



PROPOSED COMMERCIAL DEVELOPMENT

THOMAS GRAHAM LTD

**UNITS 10 & 14, BRIDGE END INDUSTRIAL ESTATE
EGREMONT**

ARBORICULTURE METHOD STATEMENT

27.02.25

Bruce Walker B Sc Hons M Phil CMLI
Chartered Landscape Architect



64 Newfield Drive, Carlisle,

Cumbria, CA3 0AF

07736 364337

bruce@westwoodlandscape.co.uk

LLP Number OC454559

CONTENTS

1 INTRODUCTION

1.1 SCOPE OF REPORT

1.2 PROPOSED WORKS AND LOCATION

2.0 ARBORICULTURE METHOD STATEMENT FOR PROTECTION OF TREES

APPENDIX

Tree Protection Fence Detail
Tree Protection Plan L02

1 INTRODUCTION

1.1 SCOPE OF REPORT

1.1.1 This report will provide an Arboriculture Method Statement to BS5837 in response to a request by Cumberland Council in connection with Planning Application number 4/24/2429/0F1. (Alistair Hearn Tree Officer and Christie M Burns, Planning Officer dated 12 February 2025).

1.1.2 Westwood Landscape Design LLP, Chartered Landscape Architects (with LANTRA Professional Tree Inspector Certification) were appointed in February 2025 by Architects Plus Ltd to provide an Arboriculture Method Statement for the proposed works which include a new build connection between Units 10 and 14 and new entrances and cladding to the existing units with associated external work improvements. This will ensure the protection of the trees and hedges on and adjacent to the proposed development site.

1.2. PROPOSED WORKS AND LOCATION

1.2.1. The proposal is for extension and improvement works to two industrial building on the established business park at Bridge End, Egremont. The proposed layout is indicated on the Tree Protection Plan L02. For location and context plans see below:



Site location Plan showing the site in the context of Egremont and the River Ehen.

Westwood Landscape Design LLP Ordnance Survey Licence Number TT:009737163



OS Plan showing the context of the site in relation to the woodland adjacent to the River Ehen.

Westwood Landscape Design LLP Ordnance Survey Licence Number TT:009737163



SITE

Aerial view showing the site in the context of the trees adjacent to the River Ehen.

Westwood Landscape Design LLP Ordnance Survey Licence Number TT:009737163

2.0 ARBORICULTURE METHOD STATEMENT FOR PROTECTION OF TREES

Refer to Appendix for Tree Protection Fence Detail.

2.1 Refer to Tree Protection Plan L02 for location of trees to be retained and proposed layout for the temporary Tree Protection Fence which will form a Construction Exclusion Zone (CEZ).

2.2 Protective fencing to be erected prior to the commencement of any other work to ensure that the trees and hedges are protected in accordance with British Standard 5837:2012 Trees in Relation to Construction. Such measures shall be retained for the duration of any approved works. Refer to detailed fencing drawing below in the Appendix.

2.3. Protective fencing must remain intact and in place, and protection procedures must be adhered to throughout the construction period. Removal of protective fencing should be the last job carried out on completion of the project and prior to final cultivation and seeding works and planting.

2.4. No mechanical traffic should be allowed above a tree's root zone as this could cause compaction and damage roots. No excavations of any kind to take place within the root zone area of protected trees. No materials should be stored within the RPA or

any ground level increase. No re-fuelling or any other activity which may lead to chemical spillage should be carried out within or close to the RPA. No fires to be lit within the RPA.

2.5. In certain circumstances it is possible to accommodate construction activities within the RPA distances recommended by the B.S. 5837:2012 calculation. This may be unavoidable for the proposed works but this will not necessarily lead to tree damage if this methodology is carefully followed. Intrusive work within the RPA should be restricted to one side of the tree and the protection zone extended on the other sides to compensate.

2.6. Pre-construction Stage

2.6.1. Prestart site meeting involving Architect, Contractor and potentially client and LPA representative if requested. Timing and implementation of the agreed Tree Works and installation of Tree protection measures.

2.6.2. Clearance of the required trees and pruning back canopies of retained trees which may be impacted by the development to crown raise to clear vehicular traffic and access equipment for cladding work.

2.6.3. Tree protection fence installed and LPA informed and given opportunity to inspect.

2.7. Development Stage

2.7.1. Contractors RAMS assessed by Architect and Landscape Architect/ Arboricultural Consultant.

2.7.2. Minimal dig construction method to be followed where work is unavoidable within the RPA of retained trees but the existing ground level will be maintained.

- For the permanent surface solution within the RPA of the trees adjacent to the north end of unit 10 where the proposed paving extension is within the tree RPA and to the west of Unit 10 where the new tarmac yard is proposed a permeable tarmac construction will be used within the tree RPA's to ensure unimpeded water and air penetration to the tree roots. These requirements must be verified by the Engineer following appropriate CBR tests and design.

- The tree adjacent to the north kerb of the Unit 10 car park has an RPA which will extend into the paved surface between parking bays 7 and 8. It is assumed that the proposed works will be limited to resurfacing with no new excavation for kerbs or sub-base therefore the disturbance to these trees will be minimal.

- To facilitate the construction of the footpath/ maintenance strip at the north edge of Unit 10 the existing vegetation over the area of the construction should be treated with a proprietary translocated Glyphosate based herbicide such as 'Roundup' and cut down to ground level. Remove vegetation to 25mm maximum depth.

- Excavation of the topsoil to a maximum depth of 150mm and no greater than 100mm beyond the proposed edges should be carried out carefully by hand or with an air spade within the RPA's. Any exposed tree roots should be re-covered with excavated topsoil as soon as possible or wrapped in hessian if they remain exposed. This will prevent root damage from drying out or sudden changes in temperature. The wraps should be removed before backfilling. Roots smaller than 25mm in diameter which are obstructing the work can be pruned with bypass secateurs or a handsaw except where they occur in clumps when the Arboricultural consultant must be consulted. Trial excavations using an air spade or careful hand excavation prior to detailed design will inform the position of any large roots which require protection. The depth and position of the proposed drainage plant may need to be adjusted to accommodate retained tree roots.
- Following excavation the kerb edges will be installed followed by a Terram 1000 or a similar weed suppressant membrane laid over the whole RPA area to receive 5-40mm Type 3 sub-base aggregate to ensure water and gaseous exchange is maximised. Lightly compact the base to prepare for the permeable surfacing.
- Once the final surfacing is installed topsoil should be spread to infill the void adjacent to the timber edges and to finish the ground level to a smooth profile. Any minor irregularities, lumps or hollows in the ground level will be evened out or filled in with topsoil using hand tools.
- Where construction traffic within the RPA at the site access routes is unavoidable a temporary protective track should be formed with interlocking panels (I-track system or similar) over a compressible layer of 200mm bark mulch or chipped wood. A more lightweight solution of timber boards will be suitable for pedestrian only routes. The boards must be suitable to spread the anticipated load such as heavy-duty scaffold boards.
- For re-cladding work it is assumed that powered access platforms will be required adjacent to the building which may require some crown reduction pruning to the trees adjacent to the north side of the unit 10. This should be carried out by a qualified Arborist and kept to a minimum to allow access.

2.7.3. Site inspections by the Landscape Architect/ Arboricultural Consultant is advisable as required during the works, especially if tree roots are encountered. If large tree roots are encountered the methodology will be adapted to ensure protection.

2.7.4. Removal of Protective Fencing once the main construction work is completed to allow re-surfacing and planting work within the CEZ.

Contacts:


Architect: Architects Plus Ltd

Contact: To be confirmed


Landscape Architect/ Arboriculture Consultant:

Contact: Bruce Walker, Westwood Landscape Design LLP, Carlisle Tel. Mobile 07736 364337

APPENDIX 1
Tree Protection Fence Detail

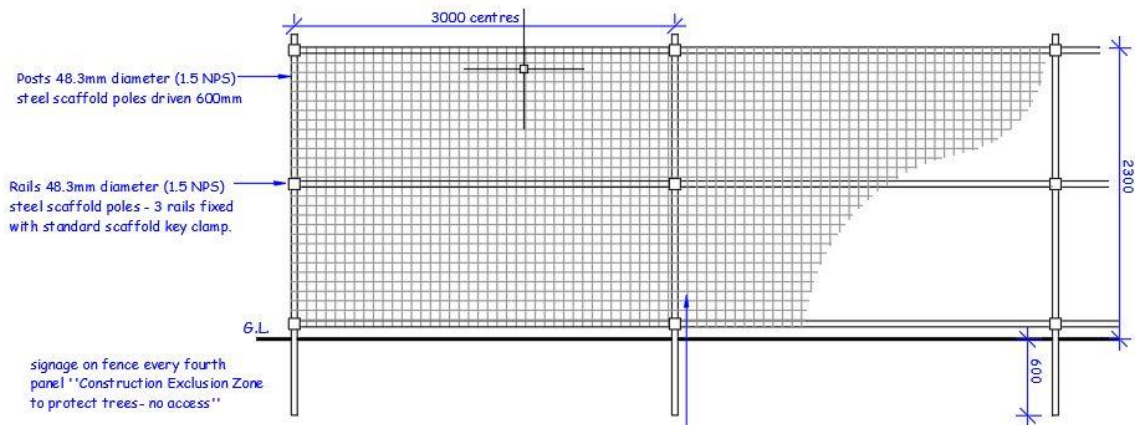

ELEVATION 1:25

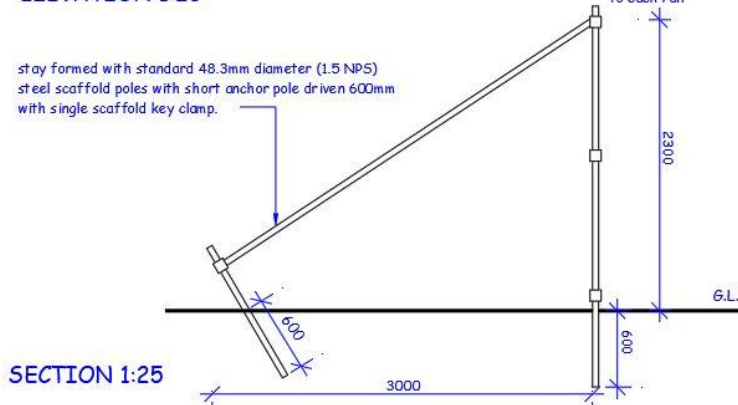

 Westwood LANDSCAPE DESIGN	
CHARTERED LANDSCAPE ARCHITECTS	
TREE PROTECTION FENCE	
DATE:	DRAWING NUMBER: WWD11
SCALE: 1:20 @ A3	
