

# Technical Note

## Arboricultural Method Statement

---

|                     |                                                                  |
|---------------------|------------------------------------------------------------------|
| <b>CLIENT:</b>      | KCS Agricultural Ltd                                             |
| <b>PROJECT:</b>     | Installation of a kest and drain at North Rheda Park, Frizington |
| <b>SUBJECT:</b>     | Arboricultural Method Statement                                  |
| <b>DATE:</b>        | 15 April 2025                                                    |
| <b>PREPARED BY:</b> | Charles Bennett – MICFor, Dip Arb L6 (ABC)                       |

### Arboricultural Method Statement

This Arboricultural Method Statement (AMS) shall be provided to the site manager and staff undertaking the works detailed below. The works must be undertaken in accordance with this AMS.

- Install Tree Protection Fencing (TPF) in accordance with the location shown on the drawing Drainage Layout 1/3 dated 23/05/2024, Ref. AA7281/EW/04, revision G dated 11.04.2025, by Asher Associates, see **Appendix A Drawings** prior to commencement of any works on site.
- The Tree protection Fencing shall be in accordance with Figure 3 b) British Standard BS5837:2012 Trees in relation to design, demolition and construction – Recommendations, see **Appendix B Tree Protection Fencing**.
- The kest and drain shall be constructed along the alignment shown in the drawing Drainage Layout 1/3 dated 23/05/2024, Ref. AA7281/EW/04, revision G dated 11.04.2025, by Asher Associates, see **Appendix A Drawings**.
- The kest and drain must be constructed to the dimensions shown in **Appendix C Kest and Drain Dimensions**.
- Only access on foot to install the kest and drain within the area protected by the TPF should occur. Outwith the fenced off area machinery can be used.
- Within the fenced off area excavate the drain to a maximum depth of 150mm using hand tools only. The spoil from the excavation is to be used to create the kest.
- Backfill the drain with gravel. Within the fenced off area gravel to be moved by hand in a wheelbarrow. No tracked or powered wheeled machinery is to be used within the fenced off area.

# Technical Note

## Arboricultural Method Statement

---

- Where spoil is to be brought in to be added to the kest to create the designed height, this is to be brought into the fenced off area using a wheelbarrow.

# Technical Note


## Arboricultural Method Statement

---

### Appendix A

#### Drawings



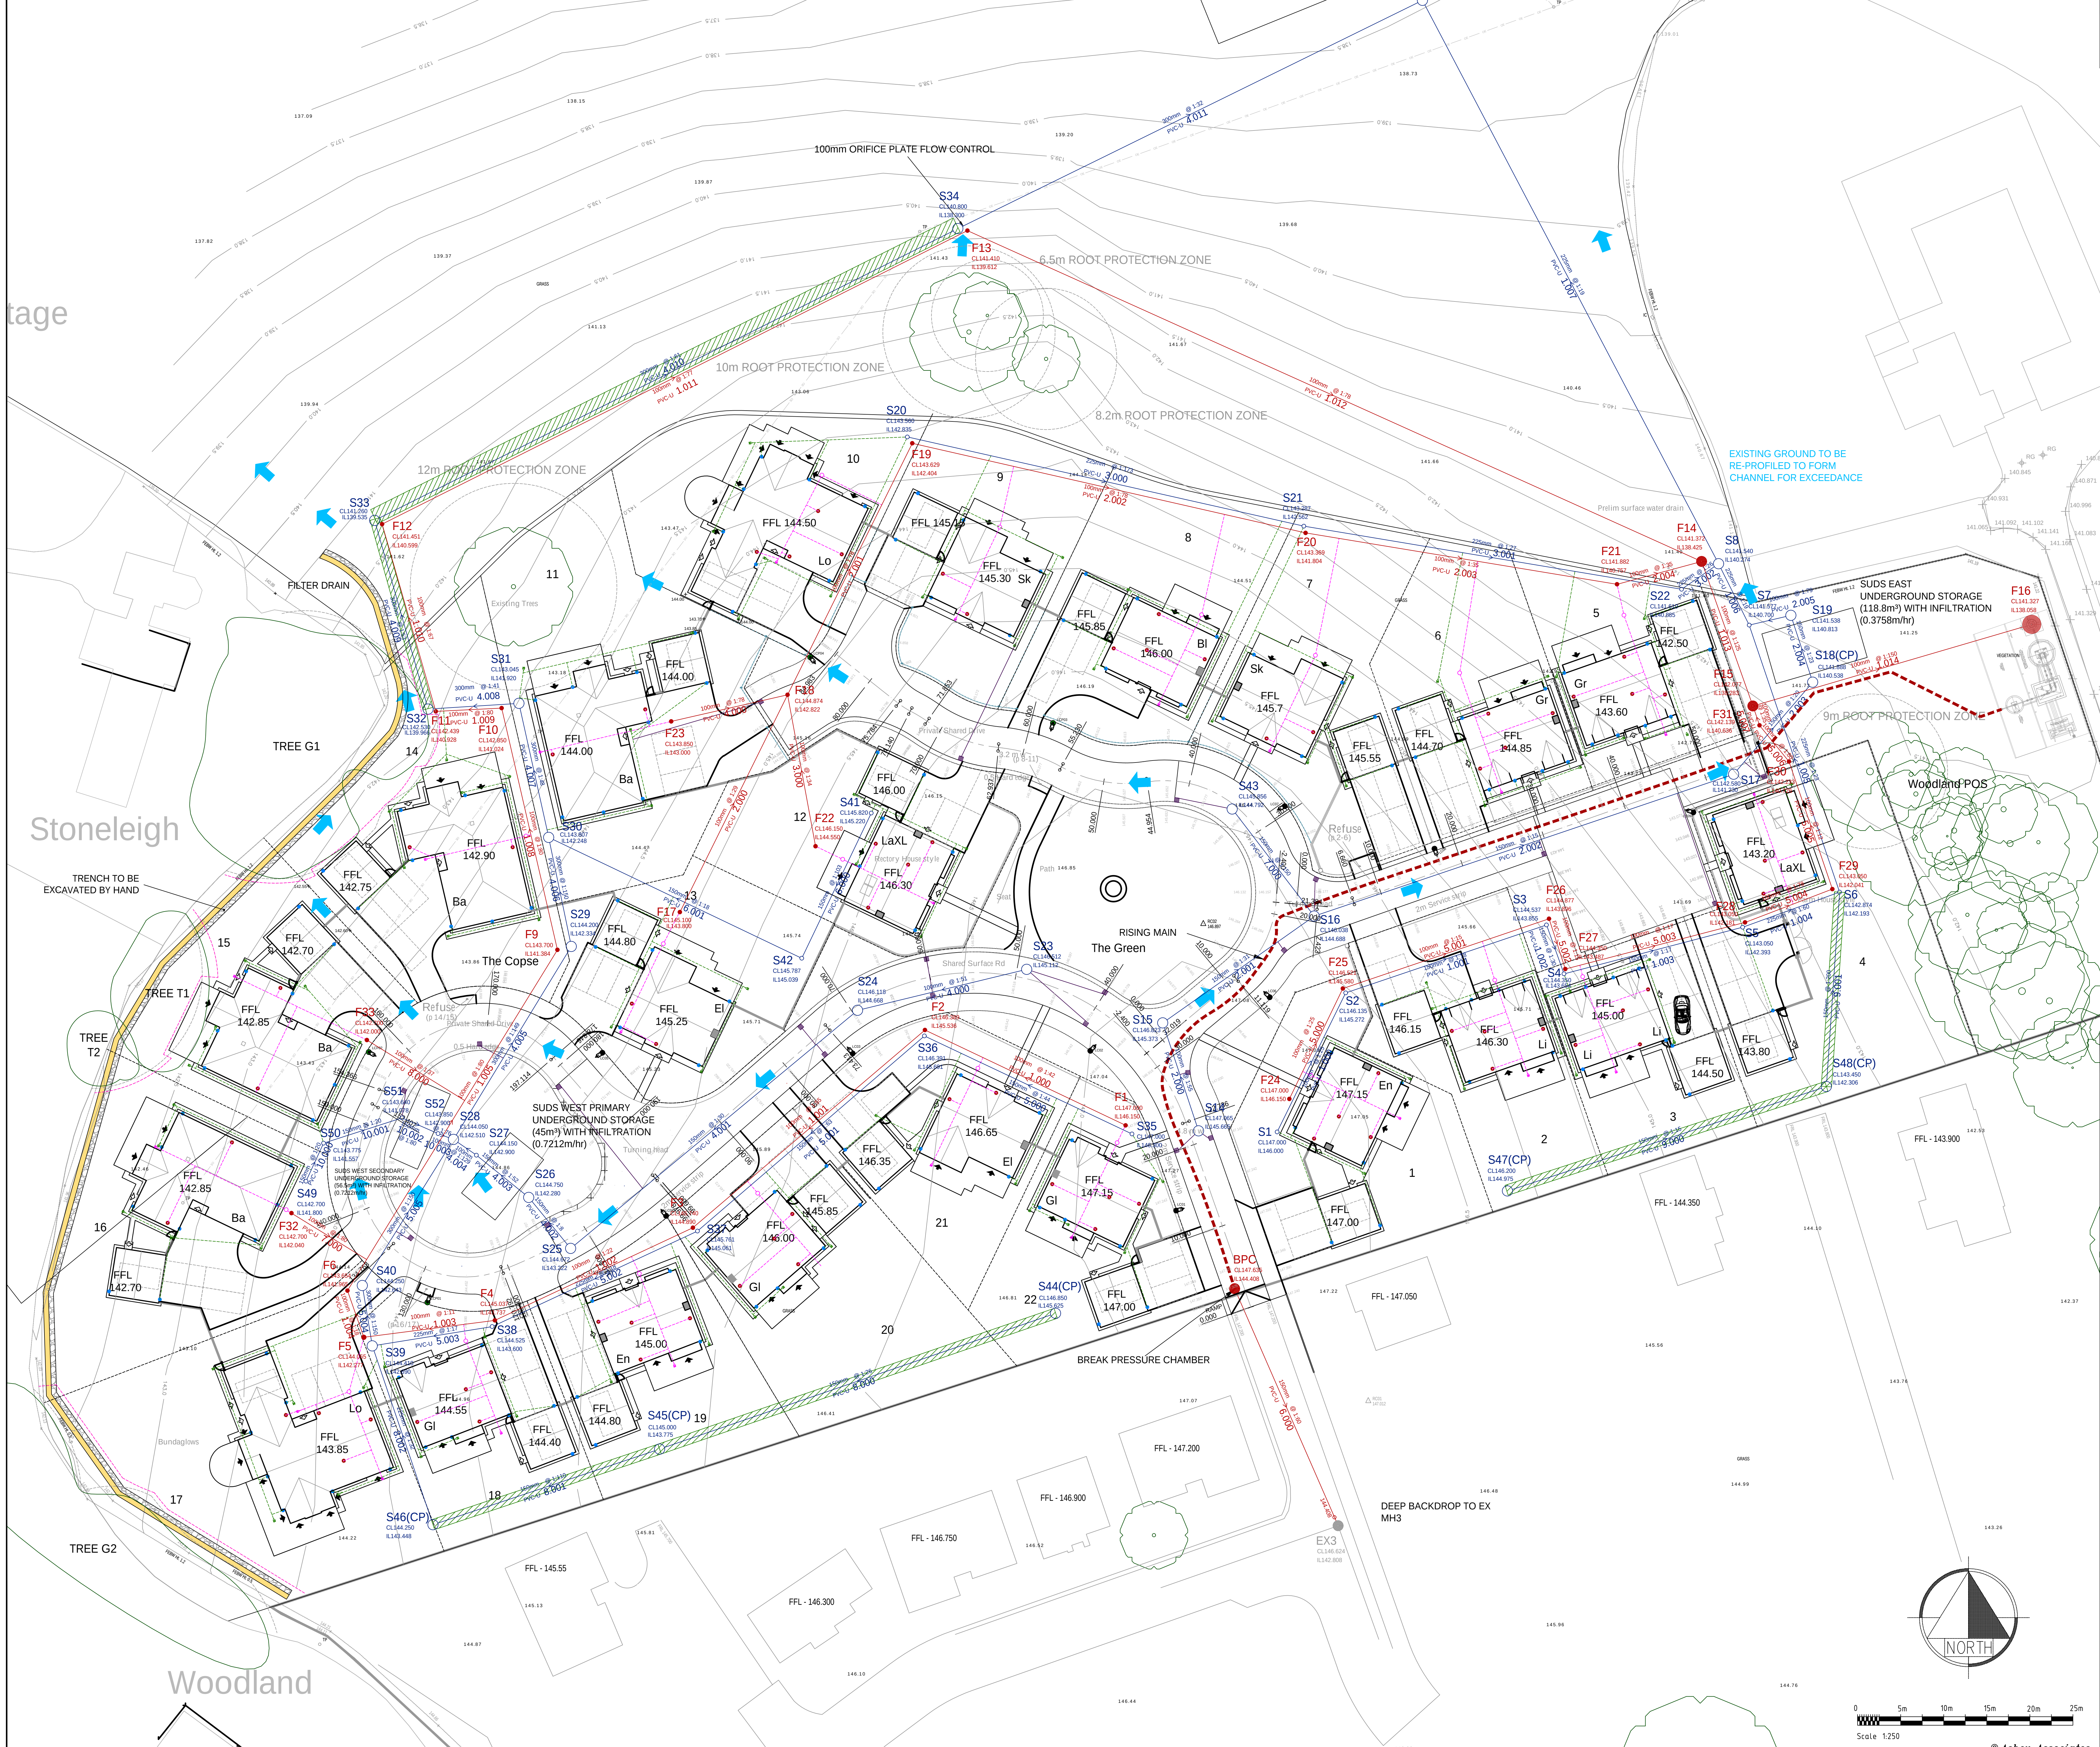

NOTES.

- DO NOT SCALE FROM THIS DRAWING.
- ALL DIMENSIONS ARE IN METRES UNLESS OTHERWISE STATED.

KEY: PROPOSED DRAINAGE

ADOPTABLE HIGHWAY DRAIN

PRIVATE SURFACE WATER DRAIN

PRIVATE FOUL SEWER

MANHOLE

MANHOLE WITH BACKDROP

CATCHPIT

HEADWALL

GULLY

CHANNEL DRAIN

SURFACE WATER INSPECTION CHAMBER

FOUL INSPECTION CHAMBER

RODDING EYE

RIISING MAIN

DRAINAGE EXCEEDANCE ROUTE

INFILTRATION TRENCH

KESTED HEDGE

ROOT PROTECTION AREA

EXISTING TREE CROWN SPREAD

TREE PROTECTION FENCING

KEY:

STREETLIGHT

PRIVATE STREETLIGHT

|                           |           |         |          |          |              |
|---------------------------|-----------|---------|----------|----------|--------------|
| Rev.                      | Amendment | By      | Checked  | Approved | Date         |
| PLANNING APPLICATION      |           |         |          |          |              |
| Status                    |           |         |          |          | Appd. Date   |
| Client                    |           |         |          |          |              |
| KCS AGRICULTURAL LTD      |           |         |          |          |              |
| Project                   |           |         |          |          |              |
| NORTH PARK RHEDA, PHASE 2 |           |         |          |          |              |
| Title                     |           |         |          |          |              |
| DRAINAGE LAYOUT 1/3       |           |         |          |          |              |
| Drawn                     | Date      | Checked | Date     | Approved | Date         |
| ROM                       | 23.05.24  | WAM     | 23.05.24 | WAM      | 23.05.24     |
| Scales                    |           |         |          |          | 1:250 @ A0   |
| Job No.                   |           |         |          |          | AA7281       |
| Client Drawing No.        |           |         |          |          |              |
| Drawing No.               |           |         |          |          | AA7281/EW/04 |
|                           |           |         |          |          | G            |

0 5m 10m 15m 20m 25m

Scale 1:250

© Asher Associates



# Technical Note

## Arboricultural Method Statement


---

Appendix B  
Tree Protection Fencing

# Technical Note

## Arboricultural Method Statement

---

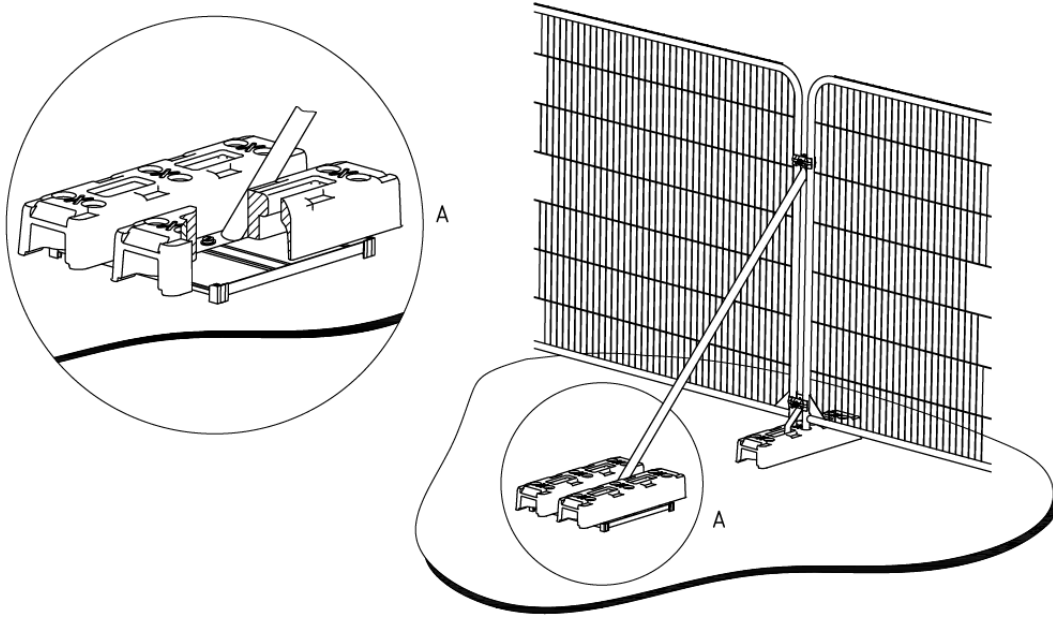

b) Stabilizer strut mounted on block tray  
Figure 3b BS5837:2012

# Technical Note

## Arboricultural Method Statement

---


### Appendix C

#### Kest and Drain Dimensions

# Technical Note

## Arboricultural Method Statement

---

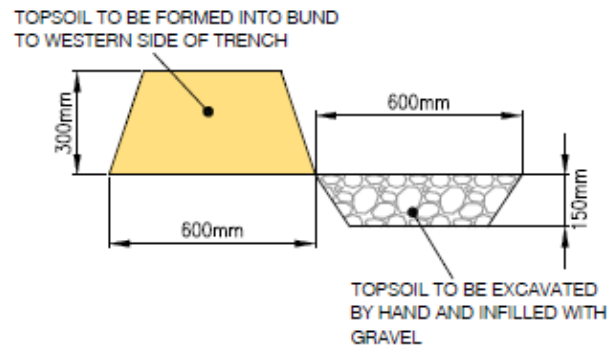

SECTION THROUGH WESTERN  
KESTED HEDGE

N.T.S



# Technical Note

## Arboricultural Method Statement

---

Charles Bennett MICFor, Dip Arb L6 (ABC)
