



Demolition Survey (with MA + PA)

Millom School
Salthouse Road
Millom
Cumbria
LA18 5AB



West Coast Surveys
Unit 2
Derwent Building
40 Lakes Road
Derwent Howe
Workington
Cumbria CA14 3YP

Contents:



Contents

1. Executive Summary [Conclusions and actions]
2. Contract Review
3. Introduction - Purpose, Aims and Objectives
4. Desk Top Review and Survey Planning
5. Survey Method
6. Exclusions and Caveats
7. Sampling and Analysis
8. Survey Results - Interpretation
9. Recommendations

APPENDICES - Survey Results

- Appendix 1 - Asbestos Register - Results
- Appendix 2 - Survey Data Sheets
- Appendix 3 - Areas Surveyed
- Appendix 4 - Analysis Certificates
- Appendix 5 - Plans

1.0 Executive summary:



Asbestos containing materials have been identified during the Demolition Survey and the specific areas are categorized below in order according to the initial Material Risk Assessment made by West Coast Surveys.

HIGH RISK MATERIALS - Material Score 10 and above or Priority Score of 18-24

Asbestos in poor condition, or asbestos debris/contamination has been identified within the following areas listed in the table below. It is recommended that risk assessment (s) are undertaken to ensure that Regulation 4, Regulation 10, Regulation 11, and Regulation 16 of the Control of Asbestos Regulations 2012 are complied with.

Building	Floor	Room	Item	Material	Risk assessment Score	Recommendations
There were no results found.						

MEDIUM RISK MATERIALS - Material Score Between 7 and 9 or Priority Score of 12-17

Asbestos containing materials, which are unsealed or damaged, have been identified within the following areas listed in the table below. It is recommended that remedial work to seal or remove these materials is undertaken as a priority and that air monitoring is carried out within adjacent areas in order to assess airborne fibre levels.

Building	Floor	Room	Item	Material	Risk assessment Score	Recommendations
Caretakers bungalow	Ground Floor	Entrance hallway G01	Brown floor tiles and adhesive	Reinforced Composite	MEDIUM (12)	A - Urgent Removal

1.0 Executive summary:



LOW RISK MATERIALS - Material Score 6 and below or Priority Score of less than 11

Asbestos Containing Materials have been identified which are in good condition, A management policy and plan need to be implemented to manage these materials safely. The materials require labelling and the condition of these materials re-inspected at 6 monthly intervals.

Building	Floor	Room	Item	Material	Risk assessment Score	Recommendations
Caretakers bungalow	Ground Floor	Bathroom G02	Bitumen adhesive	Reinforced Composite	LOW (9)	D - No Attention Required, Label
Caretakers bungalow	Ground Floor	Room 1 G06	Bitumen adhesive	Reinforced Composite	LOW (9)	D - No Attention Required, Label
Caretakers bungalow	Ground Floor	Kitchen G03	Bitumen adhesive to concrete floor	Reinforced Composite	LOW (9)	D - No Attention Required, Label
Caretakers bungalow	External	Roof E01	Soffit material	Asbestos Cement	VERY LOW (6)	D - No Attention Required, Label
Caretakers bungalow	External	Rainwater goods E02	Cement downpipe	Asbestos Cement	VERY LOW (6)	D - No Attention Required, Label

1.0 Executive summary:

PRESUMED ASBESTOS/NO ACCESS AREA

Asbestos Containing Materials have been presumed as being present to the following areas where access could not be gained. A management policy and plan needs to identify that these areas require inspection once access can be provided. These areas require re-inspection for accessibility at 6 monthly intervals.

Building	Floor	Room/Area	Recommendation
There were no results found.			

Building Notes:

Internal notes: N/A
External notes: N/A

2.0 Contract Review:



Name and address of site:	Millom School, Salthouse Road, Millom, Cumbria		
Name and address of client:	Thomas Armstrong Ltd, Workington Road, Flimby, Maryport		
Client contact:	Christine Brwon		
Type of survey:	Demolition Survey (with MA + PA)		
Date of survey:	28 Oct 2024		
Report Revision Number:	1		
TEAMS internal job number:	J002100		
Lead surveyor[s]:	Paul Agnew	Signature:	
Technically reviewed by:	Neil Murray	Signature:	
Report issue date:	19 Nov 2024		

3.0 Introduction/Objectives:



West Coast Surveys received an order of confirmation to undertake a Demolition Survey from Thomas Armstrong Ltd. This order has been accepted on the basis of the original quotation and our terms and conditions of business.

The order relates to a Demolition survey of:

Millom School
Salthouse Road
Millom
Cumbria
LA18 5AB

The survey was carried out by Paul Agnew.

The Type of survey selected / requested by the client was a Demolition survey.

The reason for selecting this survey is to enable the client to identify asbestos in his premises so that it can be removed prior to demolition.

The survey has included the completion of priority assessment in accordance with HSG227. This priority assessment was completed with input from the duty holder and his representatives.

This survey was carried out in accordance with documented in house procedures, which are based on the HSE Guidance document HSG 264.

3.1 Purpose of Survey

The purpose of this Demolition Survey is to help the duty holder identify asbestos in these premises, prior to. It provides sufficient information to help the tendering process for removal works prior to any work starting. However it is strongly recommended that any asbestos removal should be undertaken against a detailed specification. We further recommend the appointed removal contractor should attend the site to confirm for themselves the quantities and location of asbestos to be removed, prior to costing.

3.2 Aim of Survey

The aim of the survey was to;

1. Locate and record the location, extent, and product type as far as reasonably practicable of known or presumed ACM's.
2. Inspect and record information on the accessibility, condition and surface treatment of know or presumed ACM's
3. Determine and record the asbestos type based on sampling or by making a presumption based on product type and appearance
4. Locate all ACM's within the fabric of the building prior to demolition.

3.0 Introduction/Objectives(Cont):

- Type of Survey



3.3 Type of Survey – Demolition Survey

The purpose of this demolition survey is to identify ACM's to be removed prior to any demolition work being carried out. This type of survey is used to locate and describe as far as is reasonably practicable all ACM's in the whole building if demolition is planned.

Demolition surveys are intended to locate all asbestos within the building. It is a disruptive, fully intrusive survey that involves destructive inspection techniques that penetrate the building structure extensively. This involves breaking into floors, through walls, into wall voids ceilings, cladding, boxing, as necessary to gain access to all areas, including the inner fabric of the building. A full sampling programme is undertaken to identify possible ACM's and estimate their quantities.

The survey is designed to be used to help the tendering process, and should be used to start generating a specification for tendering the removal of ACM's from the building prior to demolition.

Whilst all asbestos materials have been identified as far as is reasonably practicable, some asbestos materials may remain unidentified buried within the fabric of the building during the survey. Asbestos shuttering buried within concrete slabs, asbestos hidden by structural supports, asbestos hidden behind other asbestos products, and building structures which are unsafe to fully access are potential locations.

It must be presumed that asbestos may remain unidentified to these type of areas and if suspect materials are uncovered during demolition then samples should be taken for analysis.

4.0 Desk Top Review and Survey Planning:



Details of information requested from the Duty Holder by West Coast Surveys in order to carry out a desk top review and plan the survey in accordance with HSG 264 were recorded on our pre-survey questionnaire, along with details of all the information that were provided by Christine Brwon on behalf of the client.

The Information provided was assessed during the desktop review and a survey plan, and risk assessment was produced for the survey of:

Millom School
Salthouse Road
Millom
Cumbria
LA18 5AB

The survey was carried out to [Millom School, Millom], [LA18 5AB].

Where information was provided regarding the presence of known or presumed asbestos materials then this has been validated during the course of the survey, and recorded within this report.

Detailed drawing were not provided by the client at the time of the survey.

A decontamination unit was not needed onsite during the survey.

Utilities and services were still live at the time of the survey.

Access equipment for working at heights was not required.

The survey did not involve confined space working.

The client did not inform [West Coast Surveys Ltd] of any chemical/biological hazards.

5.0 Survey Method



5.1 This survey has been undertaken in accordance with HSG264 and West Coast Surveys in house procedures.

5.2 Clients of West Coast Surveys that have signed our terms and conditions are deemed to have agreed, and accepted, our surveying approach, our sampling strategy, and our standard planning, surveying and reporting format unless they have made specific requests to the contrary.

5.3 The information provided by the client or their representative are recorded in the planning document and has been used to define the scope of the survey.

5.4 Photographs of suspected ACM's will be taken at the time of the survey unless the client expressly requests otherwise. Sampling points and suspected ACM's will not be identified with labels unless the client expressly requests otherwise.

5.5 All fibrous materials and item will be included in the survey unless, in the surveyors professional opinion, these items can be excluded (eg. Wood, wallpaper, man-made mineral fibre). Samples of all thermoplastic floor coverings will be taken unless, in the surveyors professional opinion, such items can be excluded. All textured coatings and novel bituminous will be sampled.

5.6 Areas that could not be accessed were presumed to have ACM's present until proven otherwise. Each area requiring further inspection is documented within the Executive summary (Inaccessible areas). Inaccessible areas are also shown on the plan drawings (Appendix 5)

5.7 Materials that could not be accessed and in the surveyors opinion can be dismissed will be presumed to be ACM unless proven otherwise. Materials that are not sampled but, in the surveyors opinion, have a similar appearance, location and function as a previously sampled material will be strongly presumed to be similar to the sampled material.

5.8 The quantity of samples taken may have been minimised by using 'strongly presumed' as defined above. Materials that are 'strongly presumed' to be similar to a material that has already been sampled will be recorded in the comments section of the survey and referenced against the original sampled material.

5.9 Our surveyor has made every attempt to avoid causing damage during the management surveys whilst attempting to identify possible ACM's. Minor repairs will be made and any areas accessed will be left in a safe condition.

5.10 Intrusive damage that is required to gain access to an area/location that is within the scope of the survey has been agreed with the client or the clients representative. Any remedial action will be put in place before such action is attempted. If remedial action cannot be arranged, no attempt to access the area will be made and the reasons recorded. The area/location will be presumed to have ACM's present until proven otherwise.

5.11 Non fibrous materials and item known not to contain asbestos (eg Breeze block, plaster, plasterboard plastics and non textured paints) will be excluded from the survey unless the surveyor suspects that these materials have been contaminated with asbestos from other sources or specifically requested by the client.

5.12 Older electrical equipment, which cannot be shown to contain ACM's, has been presumed to have ACM's present unless, in the surveyors professional opinion, such items can be excluded.

6.0 Exclusions and Caveats:



6.1 For safety reasons it is not possible to inspect internal areas of plant and machinery.

Access to internal wall linings and general cavities was restricted to avoid excessive damage to surface finishes.

Where areas have been designated as 'no access' or 'restricted access', unless further inspection/sampling proves otherwise, the presumption has been made that these structures/areas contain asbestos materials.

During the course of the survey it may not have been possible to access all areas of the site. Details of areas requiring further access are identified within the Data Sheets of this report. In accordance with HSG 264, asbestos is presumed to be present within these areas and should be treated accordingly until further inspection and analysis of building fabric and services proves otherwise.

It is recommended that further intrusive inspection and sampling be carried out where site refurbishment, maintenance, or similar may disturb Asbestos Containing Materials that have remained inaccessible during this survey, this should be a refurbishment/demolition survey as described in HSG 264.

Residual asbestos material may be present beneath re-lagged services and cannot be detected unless the re-lagging is systematically removed. Caution should therefore be taken when working on such materials for the potential presence of asbestos residue.

Textured Coatings such as "Artex" may contain a trace quantity of Chrysotile asbestos. Due to this low asbestos content, applications of this product may be non-homogenous and may elicit both positive and negative samples. Where both positive and negative samples are obtained the client should presume that the textured coating contains Chrysotile throughout even though a non-detected result has been obtained.

This report does not include investigations into land contamination associated with asbestos or any other contaminant.

6.2 Specific caveats

Underground services were not included in the survey.

7.0 Sampling and Analysis:



7.1 The object of bulk sampling is to identify the nature and extent of any visible ACM.

7.2 Bulk sampling is undertaken inline with the recognised safe procedures in order to cause minimal possible nuisance and potential risk to health of the building occupants and visitors. Bulk samples are taken in accordance with documented in house procedures, following guidelines detailed in HSG264 'The Survey Guide' and HSG248 'The Analyst Guide'. The quantity of samples taken will be minimised by using 'strongly presumed'. Materials that are 'strongly presumed' to be similar to a material that has already been sampled will be recorded in the comments section of the survey record and referenced against the original sampled material.

7.3 Bulk samples are returned to the appointed bulk analysis laboratory with the appropriate sample / report reference number. Where appropriate; a label will be left on site adjacent to the sample location.

7.4 The label will indicate the sample number and the date taken. This label can be used along with the report for cross reference purposes.

7.5 Bulk sample analysis is carried out in accordance with HSE document HSG 248 'The Analysts Guide' and West Coast Surveys documented in-house methods. Samples are examined under a low magnification stereomicroscope and the fibres teased apart. The fibres are then mounted in liquids of known refractive indices and examined under high magnification using polarised light and dispersion staining in accordance with HSG 248 'The Analysts Guide'.

7.6 The bulk sample description and analysis results can be found in Appendix 4 of this report – The analysis certificate.

Key to Analysis Results:

Chrysotile - White Asbestos

Amosite - Brown Asbestos

Crocidolite - Blue Asbestos

Tremolite - Rare Asbestos

Actinolite - Rare Asbestos

Anthophyllite - Rare Asbestos

8.0 Survey Results - Interpretation:

Survey Results

- 8.1** The results of the survey inspections and sampling undertaken are recorded on the enclosed Survey Data Sheets (appendix 2), Asbestos Register (appendix 1) and Non-Asbestos Material Register (appendix 3). Where asbestos containing material have been identified or presumed to be present then a Material Assessment Algorithm has been calculated as detailed in HSG 264 and reproduced in the table below:
- 8.2** Within the survey data sheets the individual scores in brackets, for each sample variable, are added together to form the final material/priority risk assessment algorithm score.

8.0 Survey Results - Interpretation (cont):



Material Risk Assessment Algorithm

Product type [or debris from product]

Score	Examples of scores
1	Asbestos reinforced composites [plastics, resins, mastics, roofing felts, vinyl floor tiles, semi- rigid paint, decorative finishes and asbestos cement etc]
2	Asbestos insulating board, mill boards, other low-density boards, textiles, gaskets, ropes and woven materials and asbestos paper.
3	Thermal insulation [e.g. pipe and boiler lagging], sprayed asbestos, loose asbestos, asbestos mattresses and packing.

Extent of damage/deterioration

Score	Examples of scores
0	Good condition: no visible damage
1	Low damage: a few scratches or surface marks, broken edges on boards or tiles, etc.
2	Moderate damage: significant breakage of materials or several small areas where material has been damaged exposing fibrous edges.
3	High damage or deterioration of materials, sprays and thermal insulation. Visible asbestos contamination by debris or residues.

Surface treatment

Score	Examples of scores
0	Composite materials containing asbestos, reinforced plastics, resins, vinyl tiles
1	Enclosed sprays or insulation, AIB [with exposed face encapsulated], cement sheets, etc.
2	Unsealed AIB, encapsulated insulation and sprays.
3	Unsealed insulation and sprays.

Asbestos Type

Score	Examples of scores
1	Chrysotile
2	Amphibole asbestos (excluding Crocidolite)
3	Crocidolite

Priority Risk Assessment Algorithm

Assessment Factor		Score	Examples of score variables
Normal occupant activity	Main type of activity in area	0 1 2 3	Rare disturbance activity (e.g. little used store room) Low disturbance activities (e.g. office type activity) Periodic disturbance (e.g. industrial or vehicular activity which may contact ACMs) High levels of disturbance, (e.g. fire door with asbestos insulating board sheet in constant use)
	Secondary activities for area	As above	As above
Likelihood of disturbance	Location	0 1 2 3	Outdoors Large rooms or well ventilated areas Rooms up to 100m ² Confined spaces
		0 1 2 3	Usually inaccessible or unlikely to be disturbed Occasionally likely to be disturbed Easily disturbed Routinely disturbed
	Accessibility	0 1 2 3	Small amounts or items (e.g. strings, gaskets) ≤10m ² or ≤10m pipe run >10m ² to ≤50m ² or >10m to ≤50m pipe run >50m ² or >50m pipe run
		0 1 2 3	
	Extent/amount	0 1 2 3	
		0 1 2 3	
	Human exposure potential	0 1 2 3	None 1 to 3 4 to 10 >10
		0 1 2 3	Infrequent Monthly Weekly Daily
	Average time area is in use	0 1 2 3	<1 hour >1 to <3 hours >3 to <6 hours >6 hours
		0 1 2 3	
	Maintenance activity	0 1 2 3	Minor disturbance (e.g. possibility of contact when gaining access) Low disturbance (e.g. changing light bulbs in asbestos insulating board ceiling) Medium disturbance (e.g. lifting one or two asbestos insulating board ceiling tiles to access a valve) High disturbance (e.g. removing a number of asbestos insulating board ceiling tiles to replace a valve or for re-cabling)
		0 1 2 3	ACM unlikely to be disturbed for maintenance ≤1 per year >1 per year >1 per month

Material Risk Assessment Score



Risk Category	Risk	Score Range	Fibre release potential
A	HIGH	Material Score 10 and above or Priority Score of 18-24	High risk with a high potential to release fibres if disturbed
B	MEDIUM	Material Score Between 7 and 9 or Priority Score of 12-17	Medium risk with a medium potential to release fibres if disturbed
C	LOW	Material Score Between 5 and 6 or Priority score of 9-11	Low risk with and having low potential to release fibres if disturbed
D	VERY LOW	Material Score 4 and below or Priority Score of less than 8	Very low risk with and having very low potential to release fibres if disturbed

9.0 Recommendations:



9.1 To comply with and ensure that the requirements of section 2 & 3 of the Health and Safety at Work Act (as amended) 1974, the Management of Health and Safety at Work Regulations 1999, the Control of Asbestos Regulations 2012 and the Control of Substances Hazardous to Health 2002 are met, the following recommendations should be implemented:

9.2 Undertake suitable and sufficient Risk Assessments of identified asbestos containing materials against normal occupation and maintenance operations, in compliance with Regulations 3 of the Management of Health & Safety at Work Regulations 1999 and Regulation 6 of the Control of Asbestos Regulations 2012.

9.3 The findings of the survey be brought to the attention of those persons who are likely to come in contact with asbestos, in compliance with Section 2 and 3 of the Health and Safety at Work Act (as amended) 1974 and Regulation 10 of the Control of Asbestos Regulations 2012.

9.4 Implement an Asbestos Management Policy, Plan and review process in compliance Regulation 4 of the Control of Asbestos Regulations 2012.

9.5 Instigate regular inspections, to record and update details of retained asbestos containing materials.

9.6 Review the arrangement under the management plan in accordance with regulation 4 of the CAR 2012.

9.7 During the course of the survey it may not have been possible to access all areas of the site. Details of areas requiring further access are identified within the Data Sheets of this report. In accordance with HSG 264, asbestos has been presumed to be present within these areas and should be treated accordingly until further inspection and analysis of building fabric and services proves otherwise.

9.8 Where asbestos debris or asbestos in poor condition has been found it is recommended that access is restricted and or controlled to these areas in accordance with Regulation 11 and Regulation 16 of the Control of Asbestos Regulations 2012.

9.9 If we have identified asbestos materials in poor condition, it is recommended that air monitoring is carried out within a number of areas where asbestos materials have been identified in order to assess airborne fibre levels within adjacent occupied areas in relation to the clearance indicator, as documented by HSG 248 the Analyst Guide.

9.10 All identified asbestos to be appropriately identified and subject to risk assessment, management, and re-inspection.

9.11 Site specific recommendations in respect to the location and condition of asbestos materials identified during the course of this inspection are detailed in the Survey Data Sheets and Asbestos register. In considering the management of asbestos materials identified to date, these recommendations should be taken into consideration.

9.12 In accordance with the Control of Asbestos Regulations 2012 the removal of ACM's fall into one of the three categories below:

Licensed Asbestos Removal

Is defined as any work, which is undertaken on a friable asbestos product or which is likely to exceed the control limit of 0.1f/cm³. A licensed asbestos removal contractor must undertake this work and a 14-day notice must be given to the HSE prior to the commencement of the work.

Notifiable Non Licensed Works

If work on an ACM causes the deterioration of the matrix material in which the asbestos fibres are firmly linked, then these works are Notifiable Non Licensed Work (NNLW). Work of this type does not require an asbestos removal licence, but the company undertaking the work must have the following:

- Notification of the work to the relevant enforcing authority prior to the work commencing.
- Medical examinations to assess each worker's state of health to be carried out, before any possible – exposure to asbestos. Then re-examinations every three years.
- Insurance for working with asbestos containing materials.
- A register of work to be kept by the employer for each employee exposed to asbestos.

Non Notifiable Non Licensed work

-Non-Licensed Works Is defined as any work, which involves short, non-continuous maintenance activities, during which only nonfriable materials are removed. It can also involve the removal of non-friable materials for refurbishment purposes. However, work of this type is only applicable where the matrix material in which the asbestos fibres are firmly linked remains intact.

- If a non-licensed contractor is appointed to undertake the removal works on the above materials, the following points must be adhered to:
- All operatives undertaking work on the material must have asbestos awareness training and practical asbestos training.

9.13 It is recommended that further intrusive investigations and sampling be carried out in accordance with HSG.264, where any major refurbishment, maintenance, installation or similar activity may expose asbestos materials that have remained inaccessible during the survey. This should be as a refurbishment/demolition survey as documented in HSG264.

9.14 The findings of this report should not be solely relied upon in obtaining costs for proposed asbestos abatement work. Any proposed abatement/removal of the asbestos should be undertaken against a detailed specification.

Appendix 1 - Asbestos Register



Building	Floor	Location /Room	S,P,SP,AS Sample No	Product Type	Condition	Surface Treatment	Asbestos Type	Quantity	Accessibility	Material Score	Priority Score	Total PA risk assessment score	Recommendation
Caretakers bungalow	Ground Floor	Entrance hallway G01, Brown floor tiles and adhesive Over concrete flooring includes electric cupboard	S CL002526	Reinforced Composite	High Damage	Completely Sealed	Chrysotile	8m²	Routinely disturbed	5	7	12	A - Urgent Removal
Caretakers bungalow	Ground Floor	Bathroom G02, Bitumen adhesive To concrete floor beneath linoleum material	S CL002528	Reinforced Composite	Low Damage	Completely Sealed	Chrysotile	4m²	Occasionally likely to be disturbed	3	6	9	D - No Attention Required, Label
Caretakers bungalow	Ground Floor	Room 1 G06, Bitumen adhesive Over concrete flooring	S CL002532	Reinforced Composite	Low Damage	Completely Sealed	Chrysotile	21m²	Easily disturbed	3	6	9	D - No Attention Required, Label
Caretakers bungalow	Ground Floor	Kitchen G03, Bitumen adhesive to concrete floor Floor	S CL002534	Reinforced Composite	Low Damage	Completely Sealed	Chrysotile	12m²	Occasionally likely to be disturbed	3	6	9	D - No Attention Required, Label
Caretakers bungalow	External	Roof E01, Soffit material To underside of roof edging to side store	S CL002535	Asbestos Cement	Good Condition	Surface Sealed	Chrysotile + Crocidolite	4lm	Occasionally likely to be disturbed	5	1	6	D - No Attention Required, Label
Caretakers bungalow	External	Rainwater goods E02, Cement downpipe Rear of side store	S CL002536	Asbestos Cement	Good Condition	Surface Sealed	Chrysotile	3lm	Easily disturbed	3	3	6	D - No Attention Required, Label

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Appendix 2 – Survey Data Sheets

Service Type	Demolition Survey		
Report Revision Number	1	Surveyors	Paul Agnew
TEAMS Job Number	J002100	Survey Date	28 Oct 2024
Site Address:	Millom School Salthouse Road Millom Cumbria LA18 5AB	Bulk Analysis Laboratory	Scopes Asbestos Analysis Services Ltd
		Sample Analysis Date	30 Oct 2024

Survey Data Sheets



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
	28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	Chrysotile (1)
	Building	Room	Item	Quantity	
	Caretakers bungalow	Entrance hallway G01	Brown floor tiles and adhesive Over concrete flooring includes electric cupboard	8m²	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
	CL002526 (S)	Reinforced Composite (1)	Completely Sealed (0)	High Damage (3)	Routinely disturbed (3)

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	3	Location	2	Number of occupants	1	Type of Maintenance	0
		Accessibility	3	Frequency of use	3	Frequency of maintenance	0
		Amount	1	Average Time	0		
Average Score	3	Average Score	2	Average Score	2	Average Score	0
Average of Priority	7						
Material Assessment Score	5						
Recommendation	A - Urgent Removal						
Surveyor comments	Found in poor condition the asbestos containing material should be removed under semi-controlled conditions by trained operatives and waste disposed of at a registered site.						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)





Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Entrance hallway G01	Walls and ceiling are plastered	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
	28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
	Building	Room	Item	Quantity	
	Caretakers bungalow	Entrance hallway G01	Modern electrics over timber backboard Electrics cupboard	N/A	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
	Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)





Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	No Asbestos Detected
Building	Room	Item	Quantity	
Caretakers bungalow	Bathroom G02	Linoleum material Over concrete flooring	4lm	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
CL002527 (S)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
	28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	Chrysotile (1)
	Building	Room	Item	Quantity	
	Caretakers bungalow	Bathroom G02	Bitumen adhesive To concrete floor beneath linoleum material	4m²	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
	CL002528 (S)	Reinforced Composite (1)	Completely Sealed (0)	Low Damage (1)	Occasionally likely to be disturbed (1)

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	2	Location	2	Number of occupants	1	Type of Maintenance	0
		Accessibility	1	Frequency of use	3	Frequency of maintenance	0
		Amount	1	Average Time	0		
Average Score	2	Average Score	2	Average Score	2	Average Score	0
Average of Priority	6						
Material Assessment Score	3						
Recommendation	D - No Attention Required, Label						
Surveyor comments	If any planned maintenance/refurbishment works would disturb the asbestos containing material, it should be removed under semi controlled conditions by registered contractors and the hazardous waste disposed of at a registered site.						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis	
	28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor		
	Building	Room	Item	Quantity		
	Caretakers bungalow	Bathroom G02	Textured coating To window wall and wall area by toilet	6m²	No Asbestos Detected	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition		
	CL002529 (S)	N/A	N/A	N/A	Accessibility	
					N/A	

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)





Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Bathroom G02	No suspect materials Bath void, Wooden panel	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
	28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
	Building	Room	Item	Quantity	
	Caretakers bungalow	Bathroom G02	Plastered boxing over wooden building support	N/A	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
	Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis	
	28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	No Asbestos Detected	
	Building	Room	Item	Quantity		
	Caretakers bungalow	Kitchen G03	Sink pad material Attached to underside of sink basin	Small amounts		
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility	
	CL002530 (S)	N/A	N/A	N/A	N/A	

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
	28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
	Building	Room	Item	Quantity	
	Caretakers bungalow	Wall cavities G04	No suspect materials found	N/A	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
	Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)





Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Kitchen G03	Modern water heater, Metal flue	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)





Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Kitchen G03	Plasterboard double layer paper covering between Ceiling	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)





Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Kitchen G03	Concrete flooring, Walls are plastered	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
	28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	No Asbestos Detected
	Building	Room	Item	Quantity	
	Caretakers bungalow	Store G05	Bitumen packer material Palletted wall area	Small amounts	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
	CL002531 (S)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:
 S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
	28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
	Building	Room	Item	Quantity	
	Caretakers bungalow	Kitchen G03	Plastered boxing over timber building support	N/A	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
	Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:
 S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)





Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Store G05	Wooden and fibreboard ceiling, Concrete and walls are brick	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
	28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	Chrysotile (1)
	Building	Room	Item	Quantity	
	Caretakers bungalow	Room 1 G06	Bitumen adhesive Over concrete flooring	21m²	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
	CL002532 (S)	Reinforced Composite (1)	Completely Sealed (0)	Low Damage (1)	Easily disturbed (2)

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	2	Location	2	Number of occupants	1	Type of Maintenance	0
		Accessibility	2	Frequency of use	3	Frequency of maintenance	0
		Amount	2	Average Time	0		
Average Score	2	Average Score	2	Average Score	2	Average Score	0
Average of Priority	6						
Material Assessment Score	3						
Recommendation	D - No Attention Required, Label						
Surveyor comments	If any planned maintenance/refurbishment works would disturb the asbestos containing material, it should be removed under semi controlled conditions by registered contractors and the hazardous waste disposed of at a registered site.						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)





Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Room 1 G06	Walls and ceiling are plastered	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)





Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	No Asbestos Detected
Building	Room	Item	Quantity	
Caretakers bungalow	Wall cavities G04	Insulation material External wall cavities	Throughout	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
CL002533 (S)	N/A	N/A	N/A	N/A


Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)

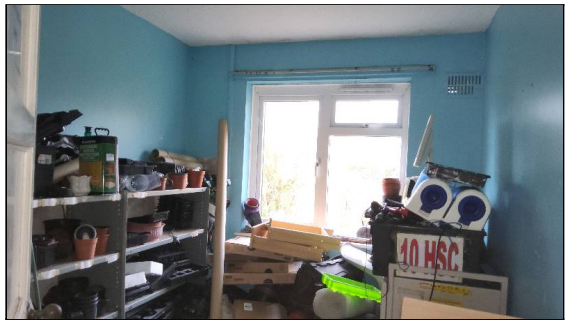

	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
	28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
	Building	Room	Item	Quantity	
	Caretakers bungalow	Room 2 G07	Wooden flooring, Walls and ceiling are plastered	N/A	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
	Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)





Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Room 3 G08	No access to floor voids due to large amount of stored items	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A


Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



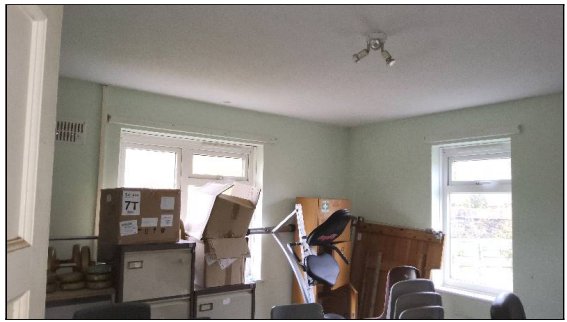

Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Room 3 G08	Wooden flooring beneath carpet, Walls and ceiling are plastered	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A


Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



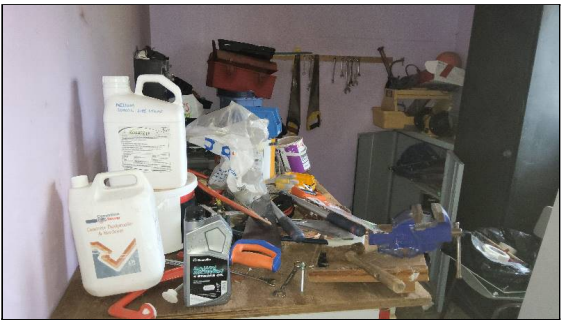

Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Room 4 G09	No access to floor void due to stored items	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)






Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Room 4 G09	No suspect materials Storage cupboard	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:
 S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



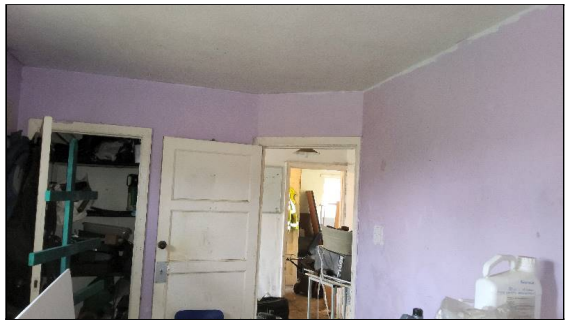

Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Room 4 G09	Wooden flooring, Walls and ceiling are plastered	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)





Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Roof Void	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Attic space R01	Modern insulation and waterproof membrane beneath roof tiles, No suspect materials visible	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
	28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	Chrysotile (1)
	Building	Room	Item	Quantity	
	Caretakers bungalow	Kitchen G03	Bitumen adhesive to concrete floor Floor	12m²	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
	CL002534 (S)	Reinforced Composite (1)	Completely Sealed (0)	Low Damage (1)	Occasionally likely to be disturbed (1)

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	2	Location	2	Number of occupants	1	Type of Maintenance	0
		Accessibility	1	Frequency of use	3	Frequency of maintenance	0
		Amount	2	Average Time	0		
Average Score	2	Average Score	2	Average Score	2	Average Score	0
Average of Priority	6						
Material Assessment Score	3						
Recommendation	D - No Attention Required, Label						
Surveyor comments	If any planned maintenance/refurbishment works would disturb the asbestos containing material, it should be removed under semi controlled conditions by registered contractors and the hazardous waste disposed of at a registered site.						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
	28 Oct 2024	Paul Agnew	Demolition Survey	External	Chrysotile + Crocidolite (3)
	Building	Room	Item	Quantity	
	Caretakers bungalow	Roof E01	Soffit material To underside of roof edging to side store	4lm	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
	CL002535 (S)	Asbestos Cement (1)	Surface Sealed (1)	Good Condition (0)	Occasionally likely to be disturbed (1)

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	0	Location	0	Number of occupants	0	Type of Maintenance	0
		Accessibility	1	Frequency of use	0	Frequency of maintenance	0
		Amount	1	Average Time	0		
Average Score	0	Average Score	1	Average Score	0	Average Score	0
Average of Priority	1						
Material Assessment Score	5						
Recommendation	D - No Attention Required, Label						
Surveyor comments	If any planned maintenance/refurbishment works would disturb the asbestos containing material, it should be removed under controlled conditions by licensed contractors and the hazardous waste disposed of at a licensed site.						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)





Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Store G05	External soffit material visible internally, Report made externally	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
	28 Oct 2024	Paul Agnew	Demolition Survey	External	Chrysotile (1)
	Building	Room	Item	Quantity	
	Caretakers bungalow	Rainwater goods E02	Cement downpipe Rear of side store	3lm	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
	CL002536 (S)	Asbestos Cement (1)	Surface Sealed (1)	Good Condition (0)	Easily disturbed (2)

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	2	Location	0	Number of occupants	0	Type of Maintenance	0
		Accessibility	2	Frequency of use	0	Frequency of maintenance	0
		Amount	1	Average Time	0		
Average Score	2	Average Score	1	Average Score	0	Average Score	0
Average of Priority	3						
Material Assessment Score	3						
Recommendation	D - No Attention Required, Label						
Surveyor comments	If any planned maintenance/refurbishment works would disturb the asbestos containing material, it should be removed under semi controlled conditions by registered contractors and the hazardous waste disposed of at a registered site.						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis	
	28 Oct 2024	Paul Agnew	Demolition Survey	External	N/A	
	Building	Room	Item	Quantity		
	Caretakers bungalow	Rainwater goods E02	Remaing guttering and downpipes are both plastic and metal	N/A		
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility	
	Visual (P)	N/A	N/A	N/A	N/A	

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
	28 Oct 2024	Paul Agnew	Demolition Survey	External	N/A
	Building	Room	Item	Quantity	
	Caretakers bungalow	Roof E01	Roof tiles are cement	N/A	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
	Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:
S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis	
	28 Oct 2024	Paul Agnew	Demolition Survey	Ground Floor	N/A	
	Building	Room	Item	Quantity		
	Caretakers bungalow	Room 1 G06	No suspect materials, Metal flue Chimney breast void	N/A		
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility	
	Visual (P)	N/A	N/A	N/A	N/A	

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)





Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	External	No Asbestos Detected
Building	Room	Item	Quantity	
Caretakers bungalow	Roof E01	Cement undercloaking material Gable roof edgings	20lm	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
CL002537 (S)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)





Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
28 Oct 2024	Paul Agnew	Demolition Survey	External	N/A
Building	Room	Item	Quantity	
Caretakers bungalow	Roof E01	Remaining soffits are plastic	N/A	
Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:	Lead Surveyor	Survey Type	Floor	Analysis
	28 Oct 2024	Paul Agnew	Demolition Survey	External	N/A
	Building	Room	Item	Quantity	
	Caretakers bungalow	Roof E01	No suspect materials Voids above soffits	N/A	
	Sample No (S,SP,P,As)	Product Type	Surface Treatment	Condition	Accessibility
	Visual (P)	N/A	N/A	N/A	N/A

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:		Lead Surveyor		Survey Type		Floor		Analysis	
	28 Oct 2024		Paul Agnew		Demolition Survey		External		No Asbestos Detected	
	Building		Room		Item		Quantity			
	Caretakers bungalow		Walls E03		Dampproof membrane Lower wall areas, Full circumference of building		Throughout			
	Sample No (S,SP,P,As)		Product Type		Surface Treatment		Condition		Accessibility	
	CL002538 (S)		N/A		N/A		N/A		N/A	

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Survey Data Sheets (cont)



	Survey Date:		Lead Surveyor	Survey Type	Floor	Analysis	
	28 Oct 2024		Paul Agnew	Demolition Survey	External	N/A	
	Building		Room	Item	Quantity		
	Caretakers bungalow		Roof E01	Modern roof felt to lower roof over side store	N/A		
	Sample No (S,SP,P,As)		Product Type	Surface Treatment	Condition	Accessibility	
	Visual (P)		N/A	N/A	N/A	N/A	

Normal Occupancy	Score	Likelihood of disturbance	Score	Exposure Potential	Score	Maintenance Activity	Score
Main type of activity	N/A	Location	N/A	Number of occupants	N/A	Type of Maintenance	N/A
		Accessibility	N/A	Frequency of use	N/A	Frequency of maintenance	N/A
		Amount	N/A	Average Time	N/A		
Average Score	N/A	Average Score	N/A	Average Score	N/A	Average Score	N/A
Average of Priority	N/A						
Material Assessment Score	N/A						
Recommendation	No further action required						
Surveyor comments	N/A						

KEY:

S – Sampled, P – Presumed, SP – Strongly Presumed, AS – Cross reference to former sample

Appendix 3 - Areas Surveyed



Building	Floor	Room No:	Room Type	Item
Caretakers bungalow	External	E01	Roof	N/A
Caretakers bungalow	External	E02	Rainwater goods	N/A
Caretakers bungalow	External	E03	Walls	N/A
Caretakers bungalow	Ground Floor	G01	Entrance hallway	N/A
Caretakers bungalow	Ground Floor	G02	Bathroom	N/A
Caretakers bungalow	Ground Floor	G03	Kitchen	N/A
Caretakers bungalow	Ground Floor	G04	Wall cavities	N/A
Caretakers bungalow	Ground Floor	G05	Store	N/A
Caretakers bungalow	Ground Floor	G06	Room 1	N/A
Caretakers bungalow	Ground Floor	G07	Room 2	N/A
Caretakers bungalow	Ground Floor	G08	Room 3	N/A
Caretakers bungalow	Ground Floor	G09	Room 4	N/A
Caretakers bungalow	Roof Void	R01	Attic space	N/A

Appendix 4 – Analysis Certificates





CERTIFICATE FOR IDENTIFICATION OF ASBESTOS FIBRES

STANDARD
PREMIUM
EMERGENCY

Client:	WEST COAST SURVEYS LTD	Analysis Report No.	SCO/24/33428			
Address:	UNIT 2, DERWENT BUILDING 40 LAKES ROAD, DERWENT HOWE WORKINGTON CUMBRIA, CA14 3YP		Report Date.	30/10/24		
Attention:	NEIL MURRAY			Site Ref No.	5776	
Site Address:	MILMOM SCHOOL SALTHOUSE ROAD MILLOM CUMBRIA, LA18 5AB		Page No:		1	Of
Date sample taken:	28/10/24	No. of Samples:		13		
Date sample received:	30/10/24		Obtained:	DELIVERED		
Date of Analysis:	30/10/24					

Samples of material, referenced below, have been examined to determine the presence of asbestos fibres, using Scopes Asbestos Analysis "in house" method of transmitted/polarised light microscopy and centre stop dispersion staining, based on HSE's HSG248. If samples have been DELIVERED the site address and actual sample location is as given by the client at the time of delivery. Scopes Asbestos Analysis Services Limited are not responsible for the accuracy or competence of the sampling by third parties. Under these circumstances Scopes Asbestos Analysis Services Limited cannot be held responsible for the interpretation of the results shown. Results relate only to the items tested.

SCOPEs SAMPLE No.	CLIENT SAMPLE No.	Sample Location	Fibre Type Detected
1	CL002526	GROUND FLOOR – ENTRANCE HALLWAY – BROWN FLOOR TILE & ADHESIVE	CHRYSTILE TO BOTH
2	CL002527	GROUND FLOOR – BATHROOM – LINOLEUM MATERIAL	NADIS
3	CL002528	GROUND FLOOR – BATHROOM – BITUMEN ADHESIVE	CHRYSTILE
4	CL002529	GROUND FLOOR – BATHROOM – TEXTURED COATING TO WALLS AREAS	NADIS
5	CL002530	GROUND FLOOR -KITCHEN – SINK PAD MATERIAL	NADIS
6	CL002531	GROUND FLOOR – STOR – BITUMEN PACKER MATERIAL	NADIS
7	CL002532	GROUND FLOOR – ROOM 1 – BITUMEN FLOOR ADHESIVE	CHRYSTILE
8	CL002533	WALL CAVITIES – INSULATION MATERIAL	NADIS
9	CL002534	GROUND FLOOR – KITCHEN- BITUMEN FLOOR ADHESIVE	CHRYSTILE

KEY: NADIS – No Asbestos Detected in Sample

Note: All samples will be retained for a minimum of six months. Reports & Records are retained for a minimum of 5 years.

Note: This Certificate for Identification of Asbestos Fibres shall not be reproduced except in full without the written approval of the Laboratory.

Note: All Analysis is performed in House on the registered premises (below).

Note: Where an 'A' appears at the end of the analysis report number this means an amendment has been made to the original report. Information that has been amended will be marked with an *

Analysed by:	T CROOT	Authorised signatory:	
		Print name:	C.BOLTON – DEPUTY Q.C.M

BULK 001-VER 8 14-JUN-22-QCM



CERTIFICATE FOR IDENTIFICATION OF ASBESTOS FIBRES

STANDARD
PREMIUM
EMERGENCY

Client:	WEST COAST SURVEYS LTD	Analysis Report No.	SCO/24/33428			
Address:	UNIT 2, DERWENT BUILDING 40 LAKES ROAD, DERWENT HOWE WORKINGTON CUMBRIA, CA14 3YP		Report Date.	30/10/24		
Attention:	NEIL MURRAY			Site Ref No.	5776	
Site Address:	MILMOM SCHOOL SALTHOUSE ROAD MILLOM CUMBRIA, LA18 5AB		Page No:		2	Of
Date sample taken:	28/10/24	No. of Samples:		13		
Date sample received:	30/10/24		Obtained:	DELIVERED		
Date of Analysis:	30/10/24					

Samples of material, referenced below, have been examined to determine the presence of asbestos fibres, using Scopes Asbestos Analysis "in house" method of transmitted/polarised light microscopy and centre stop dispersion staining, based on HSE's HSG248. If samples have been DELIVERED the site address and actual sample location is as given by the client at the time of delivery. Scopes Asbestos Analysis Services Limited are not responsible for the accuracy or competence of the sampling by third parties. Under these circumstances Scopes Asbestos Analysis Services Limited cannot be held responsible for the interpretation of the results shown. Results relate only to the items tested.

SCOPE SAMPLE No.	CLIENT SAMPLE No.	Sample Location	Fibre Type Detected
10	CL002535	EXTERNAL – ROOF – SOFFIT MATERIAL	CHRYSTILE / CROCIDOLITE
11	CL002536	EXTERNAL – RAINWATER GOODS – CEMENT DOWNPIPE	CHRYSTILE
12	CL002537	EXTERNAL – ROOF – CEMENT UNDER CLOAKING	NADIS
13	CL002538	EXTERNAL – WALLS – DAMP PROOF MEMBRANE	NADIS

KEY: NADIS – No Asbestos Detected in Sample

Note: All samples will be retained for a minimum of six months. Reports & Records are retained for a minimum of 5 years.

Note: This Certificate for Identification of Asbestos Fibres shall not be reproduced except in full without the written approval of the Laboratory.

Note: All Analysis is performed in House on the registered premises (below).

Note: Where an 'A' appears at the end of the analysis report number this means an amendment has been made to the original report. Information that has been amended will be marked with an *

Analysed by:	S GIDDINGS	Authorised signatory:	
		Print name:	C.BOLTON – DEPUTY Q.C.M
BULK 001-VER 8 14-JUN-22-QCM			

Appendix 5 – Plans



